

Weekly Update: Week of April 15, 2024

Reference: District of Ucluelet – Larch Road Active Transportation Improvements

Activities for the week of April 8 to April 12:

- Larch Road Pathway Construction (Sta. 5+200 to 5+300)
 - Common Excavation and Asphalt Removal – Ongoing
 - Existing Tree Line Trimmed 1.0m clear of MUP
 - MSE-Flex Wall Construction – Ongoing

Upcoming Activities:

- Larch Road Pathway Construction (Sta. 5+300 to 5+400)
 - Traffic Control (Temporary One-Way Street) – Refer to Traffic Management Plan
 - Common Excavation
 - MSE Walls
 - Roadway Widening
 - Installation of Base Gravels
 - *Contractor Off-Site – April 15 to April 16*

See Attached Progress Photos 1 – 6



Photo #1 – Larch Road Pathway – Roadway Widening in Progress (5+200)



Photo #2 – Larch Road Pathway – Branch Removal for Widening Completed



Photo #2 – MSE-Flex Wall Construction Ongoing (Sta. 5+300)



Photo #4 – MSE-Flex Wall Construction Ongoing (Sta. 5+300)



Photo #5 – Larch Road Pathway – Roadway Widening in Progress (5+300)

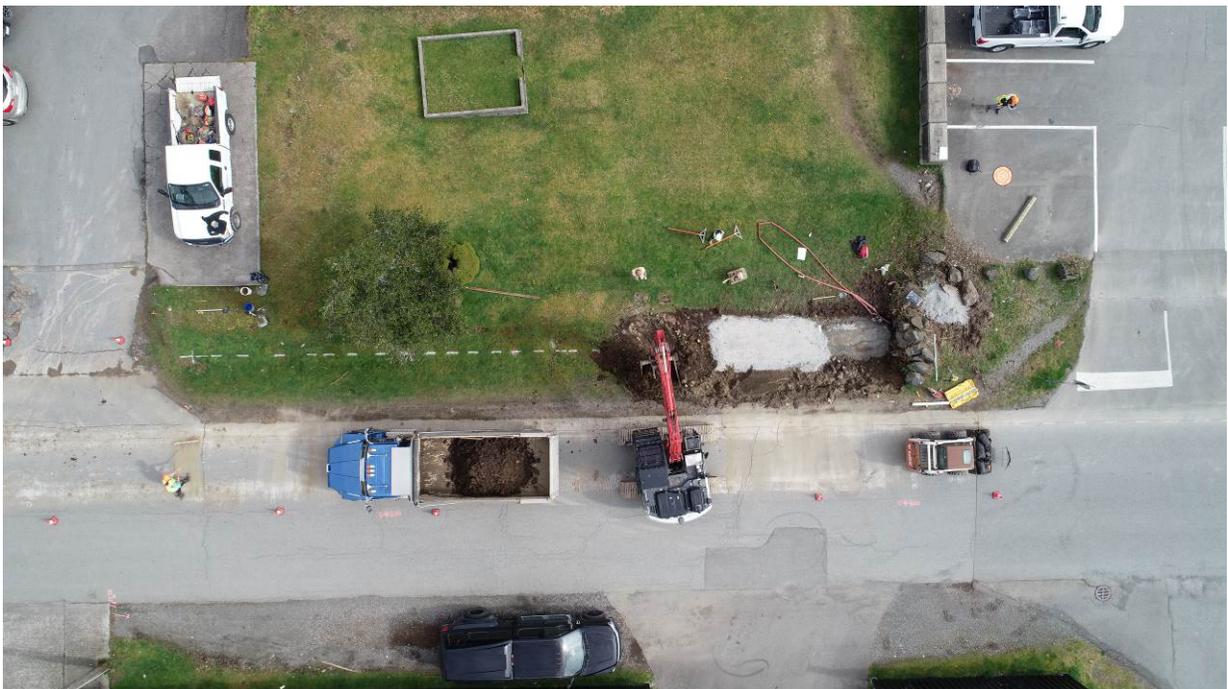


Photo #6 – Larch Road Pathway – Roadway Widening in Progress (5+300)
