

Weekly Update: Week of April 1, 2024

Reference: District of Ucluelet – Peninsula Road Improvements (Phase 1)

Activities for the week of March 25 to March 29:

- Peninsula Road Storm System Replacement
 - Contaminated Soils Removal & Disposal
 - Old Storm Pipe Removed (Along North Side of Road)
 - Catch Basin Installations Started
 - Erosion occurring at temporary connection between Existing CSP & New Concrete. Hazelwood working on improvements while waiting for manholes to be delivered.
- Larch Road Outfall
 - Final Rip Rap Placement at Outfall completed during low tide (with environmental monitor onsite)
- Pole Guy Wire Anchor Relocated by (BCH Sub-Contractor)
 - Sidewalk Guy to be installed at later date

Upcoming Activities:

- Peninsula Road Storm System Replacement
 - Peninsula Road Catch Basin – Ongoing
 - Peninsula Road Mainline (DMH #5 to DMH #6 to DMH #11) – TBC
 - Delivery expected Week of April 1
 - Bay Street Drainage Improvements – Week of April 1

Action Items:

- Sanitary System Replacement Subs – McE to provide additional information on system for Hazelwood to Price
- Peninsula Road Paving – McE to Issue CCO for Hazelwood to Price
- Progress Meeting – April 3 @ 10AM

See Attached Progress Photos 1 – 6



Photo #1 – New Catch Basins Installed



Photo #2 – Old Storm Pipe (CSP) Removed (Along North Side of Road)



Photo #3 – Old Storm Pipe (CSP) Removed (Along North Side of Road)

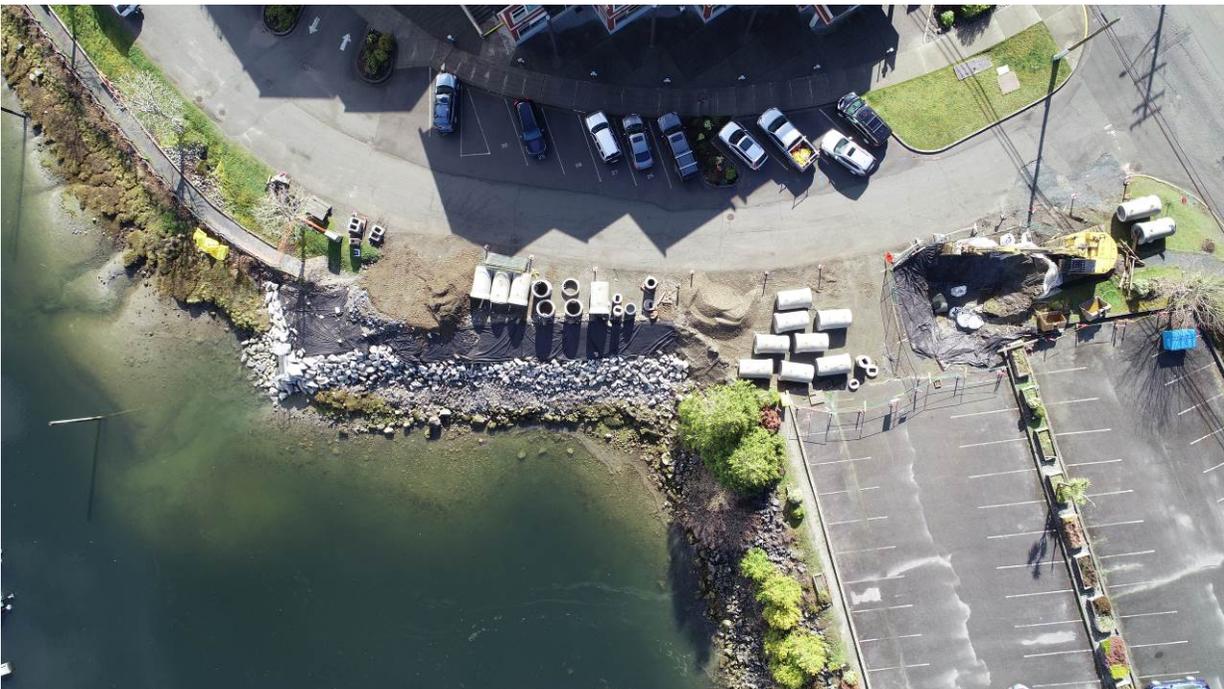


Photo #4 – Erosion occurring at temporary connection between Existing CSP & New Concrete. Hazelwood working on improvements while waiting for manholes to be delivered.



Photo #5 – Final Rip Rap Placement at Outfall completed during low tide (with environmental monitor onsite)



Photo #6 – Pole Guy Wire Anchor Relocated by (BCH Sub-Contractor)
